

Maryland Historical Trust

Maryland Inventory of Historic Properties number:

BA-2680

Name:

30171/PLEASANT GROVE RD. OVER MCGUIRE CREEK

The bridge referenced herein was inventoried by the Maryland State Highway Administration as part of the Historic Bridge Inventory, and SHA provided the Trust with eligibility determinations in February 2001. The Trust accepted the Historic Bridge Inventory on April 3, 2001. The bridge received the following determination of eligibility.

MARYLAND HISTORICAL TRUST

Eligibility Recommended \_\_\_\_\_

Eligibility Not Recommended X

Criteria:    A    B    C    D Considerations:    A    B    C    D    E    F    G    None

Comments: \_\_\_\_\_

Reviewer, OPS: Anne E. Bruder

Date: 3 April 2001

Reviewer, NR Program: Peter E. Kurtze

Date: 3 April 2001

MARYLAND INVENTORY OF HISTORIC BRIDGES  
HISTORIC BRIDGE INVENTORY  
MARYLAND STATE HIGHWAY ADMINISTRATION/  
MARYLAND HISTORICAL TRUST

MHT No. BA-2680

SHA Bridge No. B 0171

Bridge name Pleasant Grove Road over McGill Run

**LOCATION:**

Street/Road name and number [facility carried] Pleasant Grove Road

City/town Boring 0.3 mi S of Dover Road Vicinity X

County Baltimore

This bridge projects over: Road      Railway      Water X Land     

Ownership: State      County X Municipal      Other     

**HISTORIC STATUS:**

Is bridge located within a designated historic district? Yes      No X

National Register-listed district      National Register-determined-eligible district     

Locally-designated district      Other     

Name of district     

**BRIDGE TYPE:**

Timber Bridge     :

Beam Bridge      Truss -Covered      Trestle      Timber-And-Concrete     

Stone Arch Bridge     

Metal Truss Bridge     

Movable Bridge     :

Swing      Bascule Single Leaf      Bascule Multiple Leaf       
Vertical Lift      Retractable      Pontoon     

Metal Girder     :

Rolled Girder      Rolled Girder Concrete Encased       
Plate Girder      Plate Girder Concrete Encased     

Metal Suspension     

Metal Arch     

Metal Cantilever     

Concrete X:

Concrete Arch      Concrete Slab X Concrete Beam      Rigid Frame     

Other      Type Name

**DESCRIPTION:**

**Setting:** Urban \_\_\_\_\_ Small town \_\_\_\_\_ Rural X

**Describe Setting:**

Bridge B0171 carries Pleasant Grove Road in a north-south direction over McGill Run which flows in a westerly direction. The bridge is in a wooded rural area with one house approximately 100 yards from the crossing.

**Describe Superstructure and Substructure:**

Bridge B0171 is a two span concrete slab bridge measuring 25 feet in total length. The concrete wingwalls flare back along the embankment; the west walls are 10 feet long and the east walls are 8 feet long. The parapets are solid concrete. Each span is 11 feet wide and the total span between abutments is 23 feet. The clear roadway width is 29 feet and the deck out to out width is 32 feet. The road way supports two lanes of traffic. The bridge is posted for restricted load.

The 1993 inspection report describes the bridge in fair condition. The parapets are cracked and spalled, both original and replaced deck are sound although the original (east) side has 30% exposed aggregate. Both new portions of the abutments, the SW wingwall, and the NW wingwall are all in good condition, the original abutments are in fair condition with some honeycomb scaling and cracks. Erosion is severe behind all four wingwalls, the pier exhibits cracks and spalling.

**Discuss Major Alterations:**

The reinforced concrete deck was widened in 1968; as were abutments and the pier. Two new wingwalls were built.

**HISTORY:**

**WHEN was bridge built (actual date or date range)** 1920 (widened in 1968)

**This date is:** Actual X Estimated \_\_\_\_\_

**Source of date:** Plaque \_\_\_\_\_ Design plans \_\_\_\_\_ County bridge files/inspection form X

**Other (specify)** \_\_\_\_\_

**WHY was the bridge built?**

The need for a more efficient transportation network and increased load capacity in the decades following World War I.

**WHO was the designer?**

State Highway Administration

**WHO was the builder?**

Unknown

**WHY was the bridge altered?**

The bridge was reconstructed to address structural needs and safety.

**Was this bridge built as part of an organized bridge-building campaign?**

As part of an effort by the State to increase load capacity on secondary roads during the 1920s.

**SURVEYOR/HISTORIAN ANALYSIS:**

**This bridge may have National Register significance for its association with:**

**A - Events** \_\_\_\_\_ **B- Person** \_\_\_\_\_  
**C- Engineering/architectural character** \_\_\_\_\_

This bridge does not have National Register significance.

**Was the bridge constructed in response to significant events in Maryland or local history?**

Reinforced concrete slab bridges are a twentieth century structure type, easily adapted to the need for expedient engineering solutions. Reinforced concrete technology developed rapidly in the early twentieth century with early recognition of the potential for standardized design. The first U.S. attempt to standardize concrete design specifications came in 1903-04 with the formation of the Joint Committee on Concrete and Reinforced Concrete of the American Society of Civil Engineers.

Maryland's road and bridge improvement programs mirrored economic cycles. The first road improvement program of the State Roads Commission was a 7 year program, starting with the Commission's establishment in 1908 and ending in 1915. Due to World War I, the period from 1916-1920 was one of relative inactivity; only roads of first priority were built. Truck traffic resulting from war-related factories and military installations generated new, heavy traffic unanticipated by the builders of the early road system. From 1920 to 1929, numerous highway improvements occurred in response to the increase in Maryland motor vehicles from 103,000 in 1920 to 320,000 in 1929, with emphasis on the secondary system of feeder roads which moved traffic from the primary roads built before World War I. After World War I, Maryland's bridge system also was appraised as too narrow and structurally inadequate for the increasing traffic, with plans for an expanded bridge program to be handled by the Bridge Division, set up in 1920. In 1920 under Chapter 508 of the Acts of 1920 the State issued a bond of \$3,000,000.00 for road construction; the primary purpose of these monies was to meet the state obligations involving the construction of rural post roads. The secondary purpose of these monies was to fund [with an equal sum from the counties] the building of lateral roads. The number of hard surfaced roads on the state system grew from 2000 in 1920 to 3200 in 1930. By 1930, Maryland's primary system had become inadequate to the huge freight trucks and volume of passenger cars in use, with major improvements occurring in the late 1930s. Most improvements to local roads waited until the years after World War II.

With a diverse topographical domain encompassing numerous small and large crossings, Maryland engineers quickly recognized the need for expedient design and construction.

In the early years, there was a need to replace the numerous single lane timber bridges. Walter Wilson Crosby, Chief Engineer stated in 1906, "The general plan has been to replace these [wood bridges] with pipe culverts or concrete bridges and thus forever do away with the further expense of the maintenance of expensive and dangerous wooden structures". Within a few years, readily constructed standardized bridges of concrete were being built throughout the state.

The creation of standard plans and a description of their use was first announced in the 1912-15 Reports of the State Roads Commission whereby bridges spanning up to 36 feet were to use standardized designs.

Published on a single sheet, the 1912 Standard Plans included those structures that were amenable to such an approach: slab spans, (deck) girder spans, box culverts, box bridges, abutments, and piers

(State Roads Commission 1912). Slab spans, with lengths of 6 to 16 feet in two foot increments, featured a solid parapet that was integrated into the slab, with a roadway of 22 feet.

In the Report for the years 1916-1919, a revision of the standard plans was noted:

During the four years covered by this report, it has been found necessary to revise our standard plans for culverts and bridges, to take care of the increased tonnage which they have been forced to carry. Army cantonments...increased their operations several hundred per cent, and the brunt of the enormous truck traffic resulting therefrom, was borne by the State Roads of Maryland. In addition to these war activities, freight motor lines from Baltimore to Washington, Philadelphia, New York, and various points throughout Maryland, and the weight of many of these trucks when loaded, was in excess of the loads for which our early bridges were designed (State Roads Commission 1920:56).

Published on separate sheets, the new standard plans (State Roads Commission 1919) for slab bridges reveal that the major changes was an increase in roadway width from 22 feet to 24 feet and a redesign of the reinforcement. The slab spans continued to feature solid parapets integrated into the span. The range of span lengths remained 6 to 16 feet, but the next year (1920) witnessed the issue of a supplemental plan for a 20 foot long slab span (State Roads Commission 1920).

Based upon documentary evidence, Baltimore County and City were the early pioneers in concrete bridge building in Maryland. The first reinforced concrete bridge documented in Maryland was the bridge at Sherwood Station, built in 1903 by Baltimore County.

Evidence from historic maps suggests that almost all of the extant concrete slab bridges built before 1940 in Baltimore County replaced earlier bridges. With the exception of two bridges, all of these structures lie on roads whose alignments have changed little since the middle of the nineteenth century. The two exceptions are both located on Shelbourne Avenue in Arbutus. Shelbourne Avenue does not appear on the 1850 map of Baltimore County but does appear on the 1915 map. Both concrete slabs bridges on Shelbourne Avenue, however, were built after 1915. The evidence therefore suggests that these two bridges were also built to replace previous structures.

**When the bridge was built and/or given a major alteration, did it have a significant impact on the growth and development of the area?**

There is no evidence to suggest that the construction of this bridge had a significant impact on the growth and development of this area.

**Is the bridge located in an area which may be eligible for historic designation and would the bridge add to or detract from the historic/visual character of the potential district?**

The bridge is not located in an area which may be eligible for historic designation.

**Is the bridge a significant example of its type?**

No, this bridge is an undistinguished example of its type.

**Does the bridge retain integrity of important elements described in Context Addendum?**

No. The bridge was reconstructed in 1968 when the slab, abutments and wingwalls were changed.

**Is the bridge a significant example of the work of a manufacturer, designer, and/or engineer?**

The bridge is not a significant example of the work a manufacturer, designer, and/or engineer.

BA-2680

**Should the bridge be given further study before an evaluation of its significance is made?**

No additional study will be needed before an evaluation of the significance of this bridge is made.

**BIBLIOGRAPHY:**

County inspection/bridge files       X            SHA inspection/bridge files                     

Other (list):

**SURVEYOR:**

Date bridge recorded       08/15/95      


Name of surveyor       Colin Farr      

Organization/Address P.A.C. Spero & Company, Suite 412, 40 West Chesapeake Ave., Baltimore,  
MD 21204

Phone number (410) 296-1635      FAX number (410) 296-1670

Maryland Historic Highway Bridges  
Bridge Type CONCRETE SLAB  
Map COCKEYSVILLE, B-12  
County BALTIMORE  
Bridge # and Name B0171 PLEASANT GROVE ROAD OVER MCGILL RUN

BA-2680

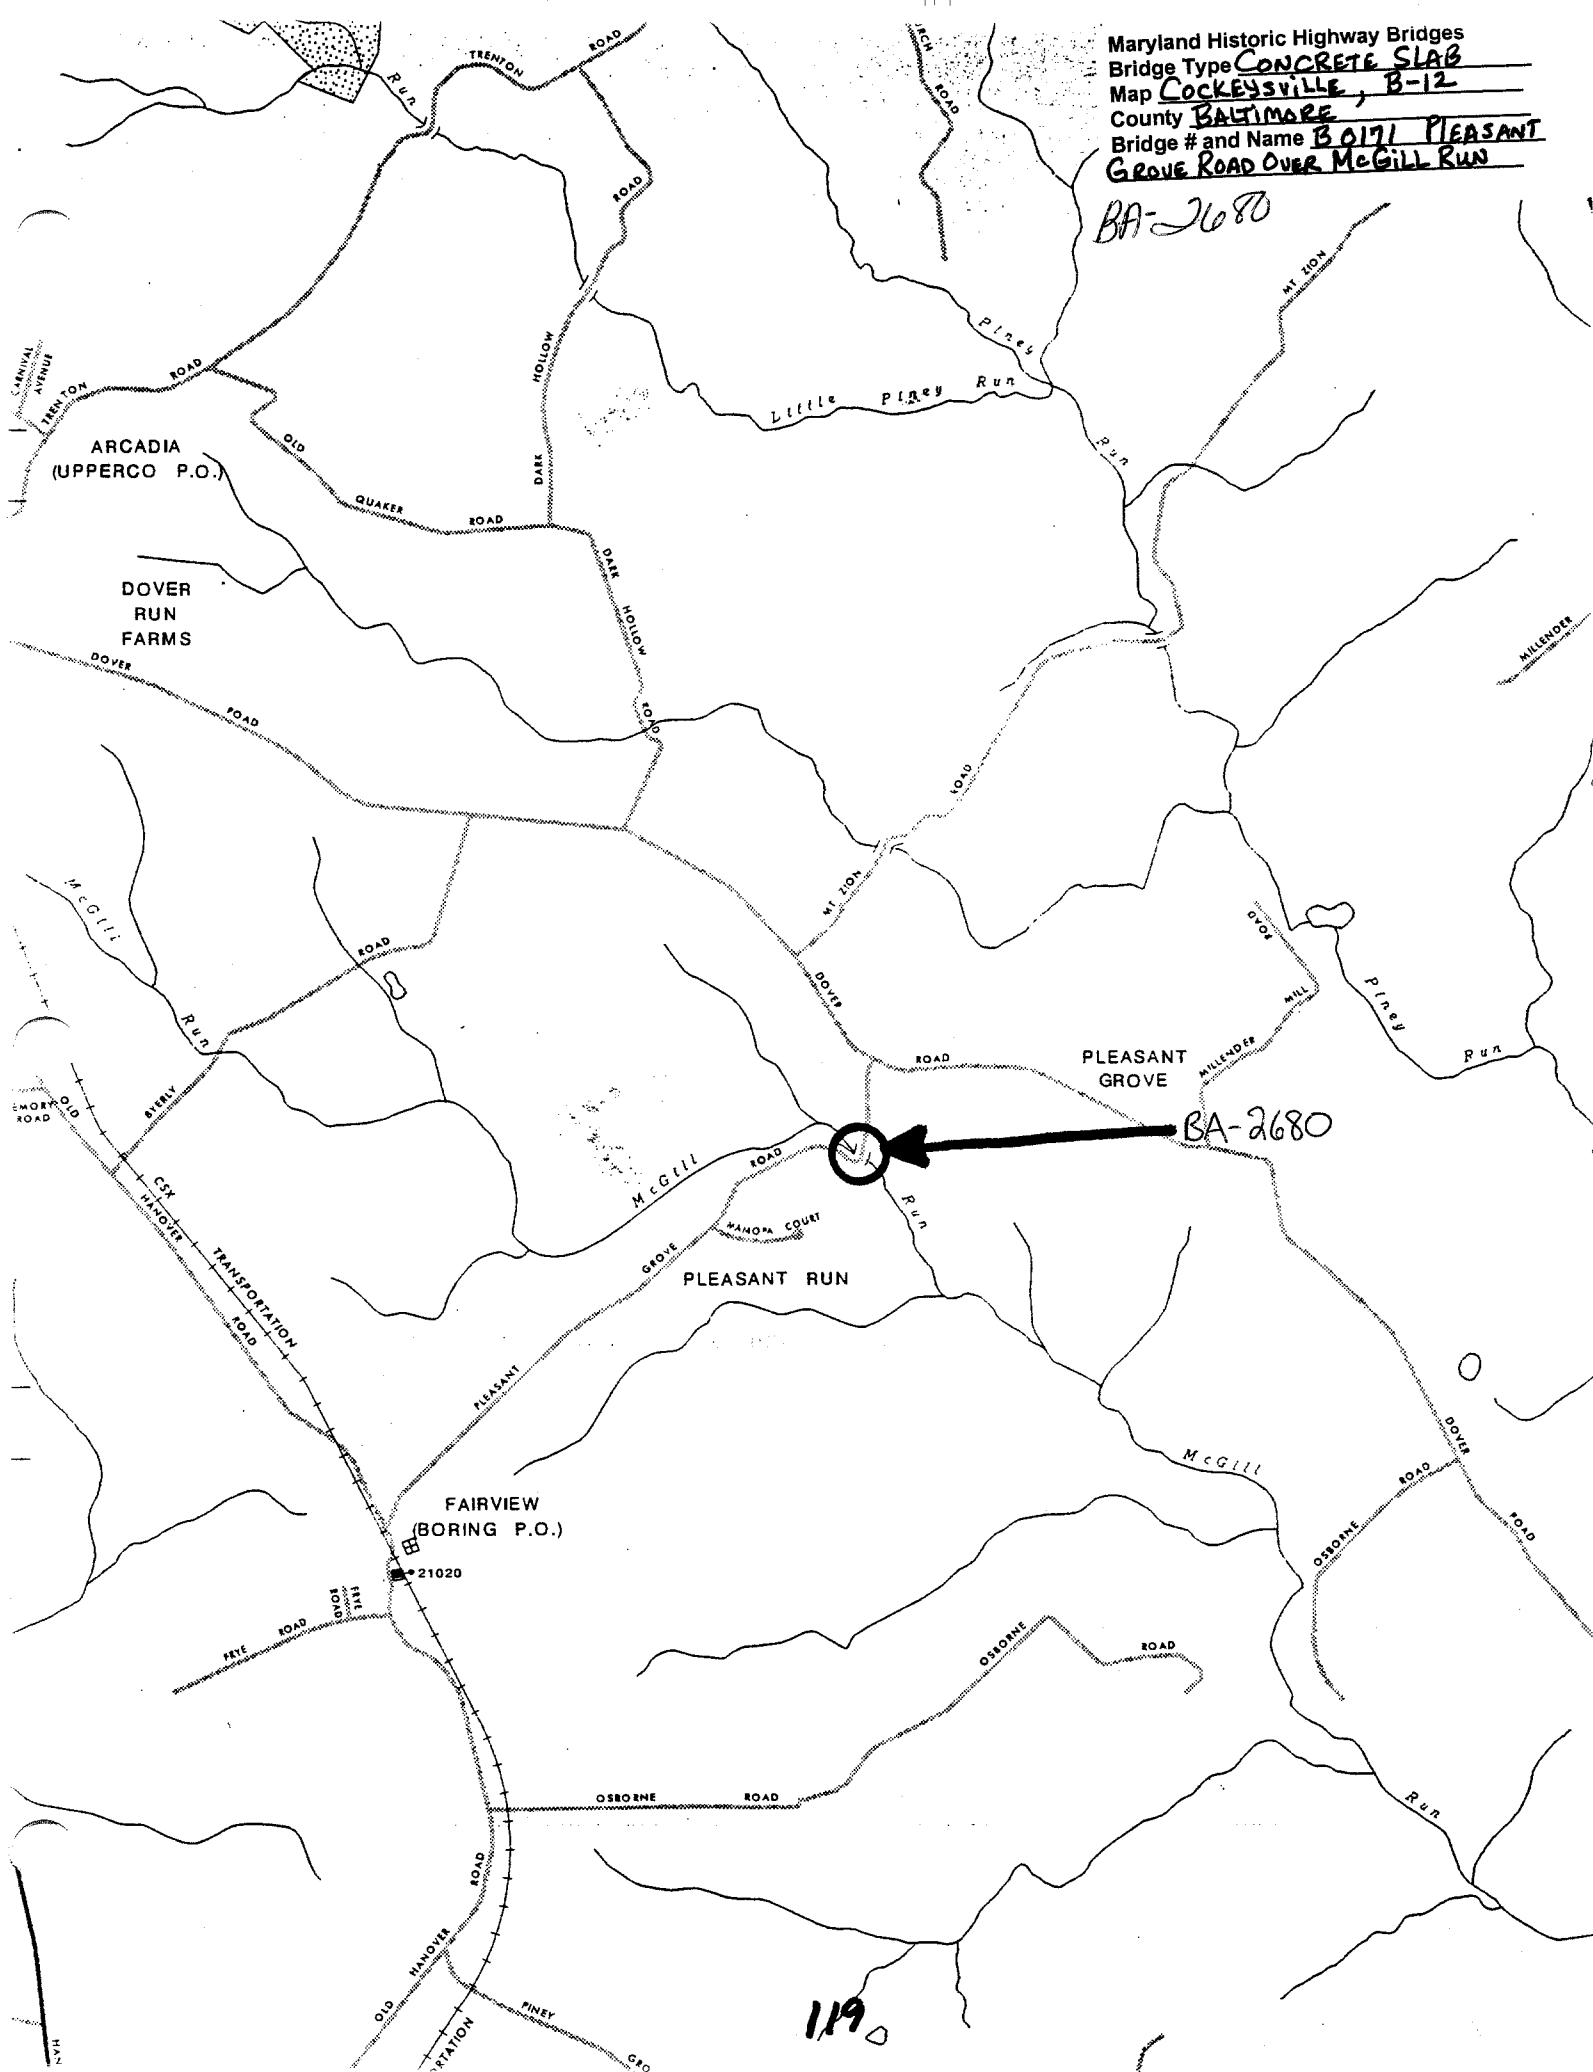





Inventory # BA-2680

Name B071- PLEASANT GROVE RD OVER MCGILL RUN

County/State BALTIMORE COUNTY / MD

Name of Photographer DAVE DIEHL

Date 1/95

Location of Negative SHA

Description SOUTH APPROACH LOOKING  
NORTHEAST

Number 14 of 344



Inventory # BA-2680

Name B0171-PLEASANT GROVE RD OVER MCGILL RUN

County/State BALTIMORE COUNTY / MD

Name of Photographer DAVE DIEHL

Date 1/95

Location of Negative SHA

Description EAST ELEVATION LOOKING  
NORTH

Number 22 of 344



Inventory # BA-2680

Name B0171-PLEASANT GROVE RD WER MCGILL RMN

County/State BALTIMORE COUNTY / MD

Name of Photographer DAVE DIEHL

Date 1/95

Location of Negative SHA

Description WEST ELEVATION LOOKING  
SOUTH

Number 3 of 34 4



Inventory # B/A 2680

Name 6071- PLEASANT GROVE RD OVER MCGILL RUN

County/State BALTIMORE COUNTY / MD

Name of Photographer DAVE DIEHL

Date 1/95

Location of Negative SHA

Description NORTH APPROACH LOOKING  
SOUTHEAST

Number 4 of 34 4
